### PBI ATCT/TRACON

Monthly Construction Stakeholder Meeting (MCSM)

#### **TWY C and A Construction**

To: PBIA Monthly Construction Stakeholder

Meeting (MCSM)


By: Robert Berlucchi ATM and Shane Ahern, FLM

Date: July 12, 2017





#### PBI Airport Diagram – New 6/24

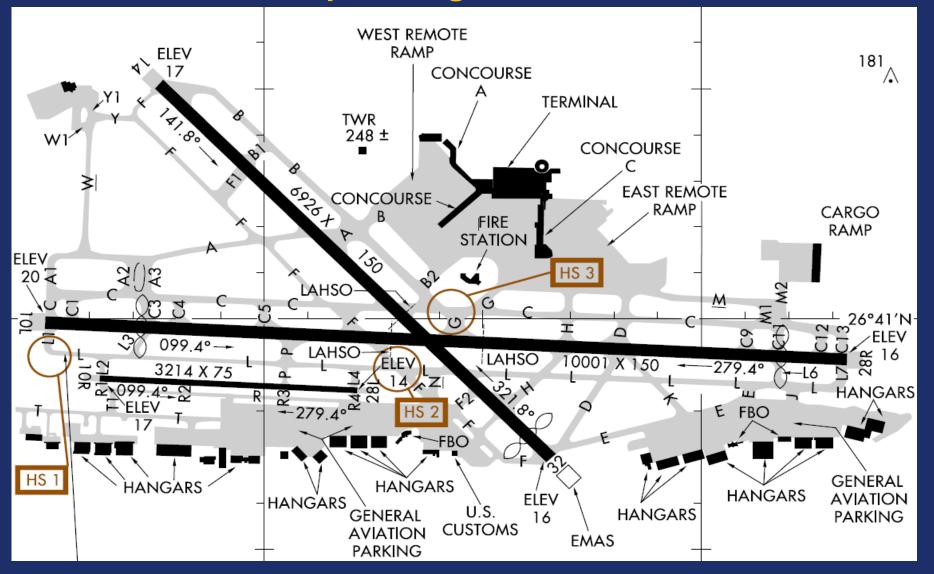



#### **PBI Playbook**

PBIA has numerous projects running simultaneously

#### **PHASES**

Phases refer only to a specific taxiway and runway.

#### **STAGES**

Stages change when a phase in one of the projects occur and changes the airport configuration.



#### **Stage Schedule and Impacts**

#### **Normal Arrival Rate East / West = 28**

Stage 8	<u>East</u> 28	<u>West</u>		
		28	June 24 – July 20	Off Peak < severe WX
Stage 9	26	26	July 10 – Aug 4	Off Peak + severe WX
Stage 10	28	28	July 21 – Aug 4	Off Peak + severe WX
Stage 11	28	26	July 21 – Aug 25	Off Peak + severe WX
Stage 12	28	24	TBD	Off Peak + severe WX
Stage 13	28	24	TBD	Off Peak + severe WX
Stage 14 (NEW)	28	24	TBD	Off Peak + severe WX



Stage 12-14 rescheduled due to ongoing weather cycle



## **Taxiway Renaming Information**



#### **Taxiway Renamed near Runway 10R**

Runway 10R is now open

Smaller GA aircraft using RWY 10R may not be familiar New Taxiways L-1, L-4, R-1, R-2, T-1

Taxiway "S" removed

New R-1 same area as TWY S - moved & new configuration



#### Taxiway Renaming Plan July 8 Runway 10R Opened









**July 10 – Aug 4** 


New Intersection Departures
RWY 14/32 closed
use for taxi at TWY C and south
Strategic Push Back Plan
Expedited Disabled Aircraft Recovery Plan



#### **West Operations**



#### STRATEGIC PUSHBACK PLAN – USE OF INNER TAXILANE

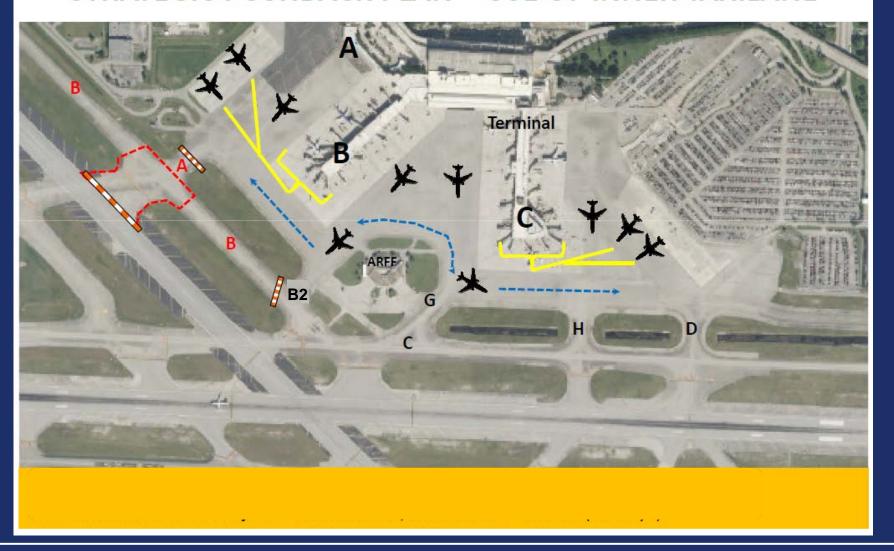

#### **Expedited Disabled Aircraft Recovery Plan**

A disabled aircraft closing RWY 10L/28R when RWY 14/32 is closed Will shut down & close operations at PBI until removed

Users should have a plan, including needed equipment, to remove their aircraft as soon as possible, if necessary


Divert aircraft may require equipment not currently at PBIA – a plan and locations of equipment should be prepared in advance

July 21 – Aug 4

New Intersection Departure at TWY C1 and TWY C2
Strategic Push Back Plan
Expedited Disabled Aircraft Recovery Plan



#### **East Operations**

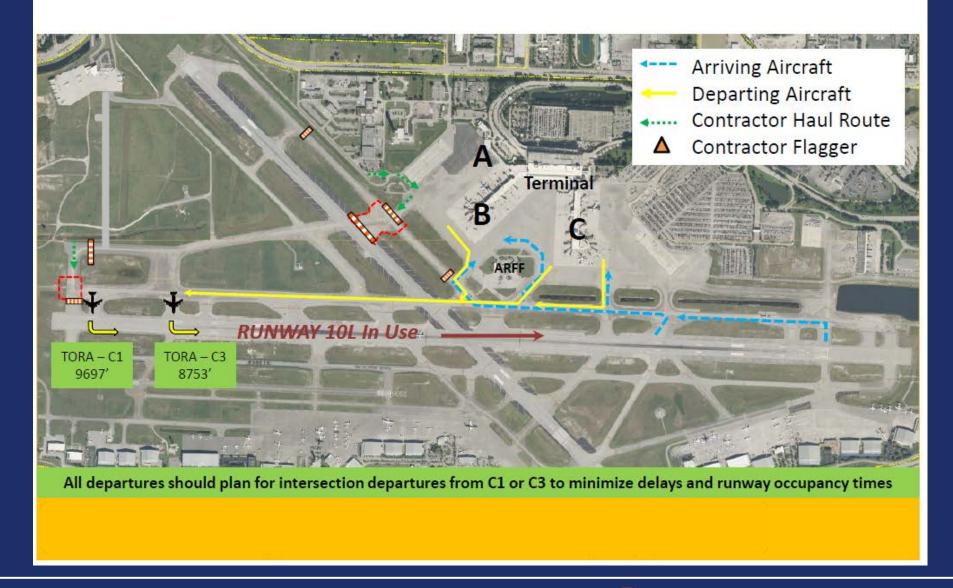

July 21 – Aug 25

#### Stage 11 Jul 21 – Aug 25



# PBI Air Traffic Airport Construction POCs

Shane Ahern, FLM

(561) 275-1405

shane.t.ahern@faa.gov

Robert Berlucchi, ATM

(561) 275-1401

robert.berlucchi@faa.gov



## Stakeholder Meetings 2nd Wednesday of each month

Next Meeting: August 9, 2017 @ 10:30 AM

See you then!

